


[illegible]

LOG OF BORING No. OW-34/1

PROJECT : MRT Orange Line Project Bang Khun Non -t

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

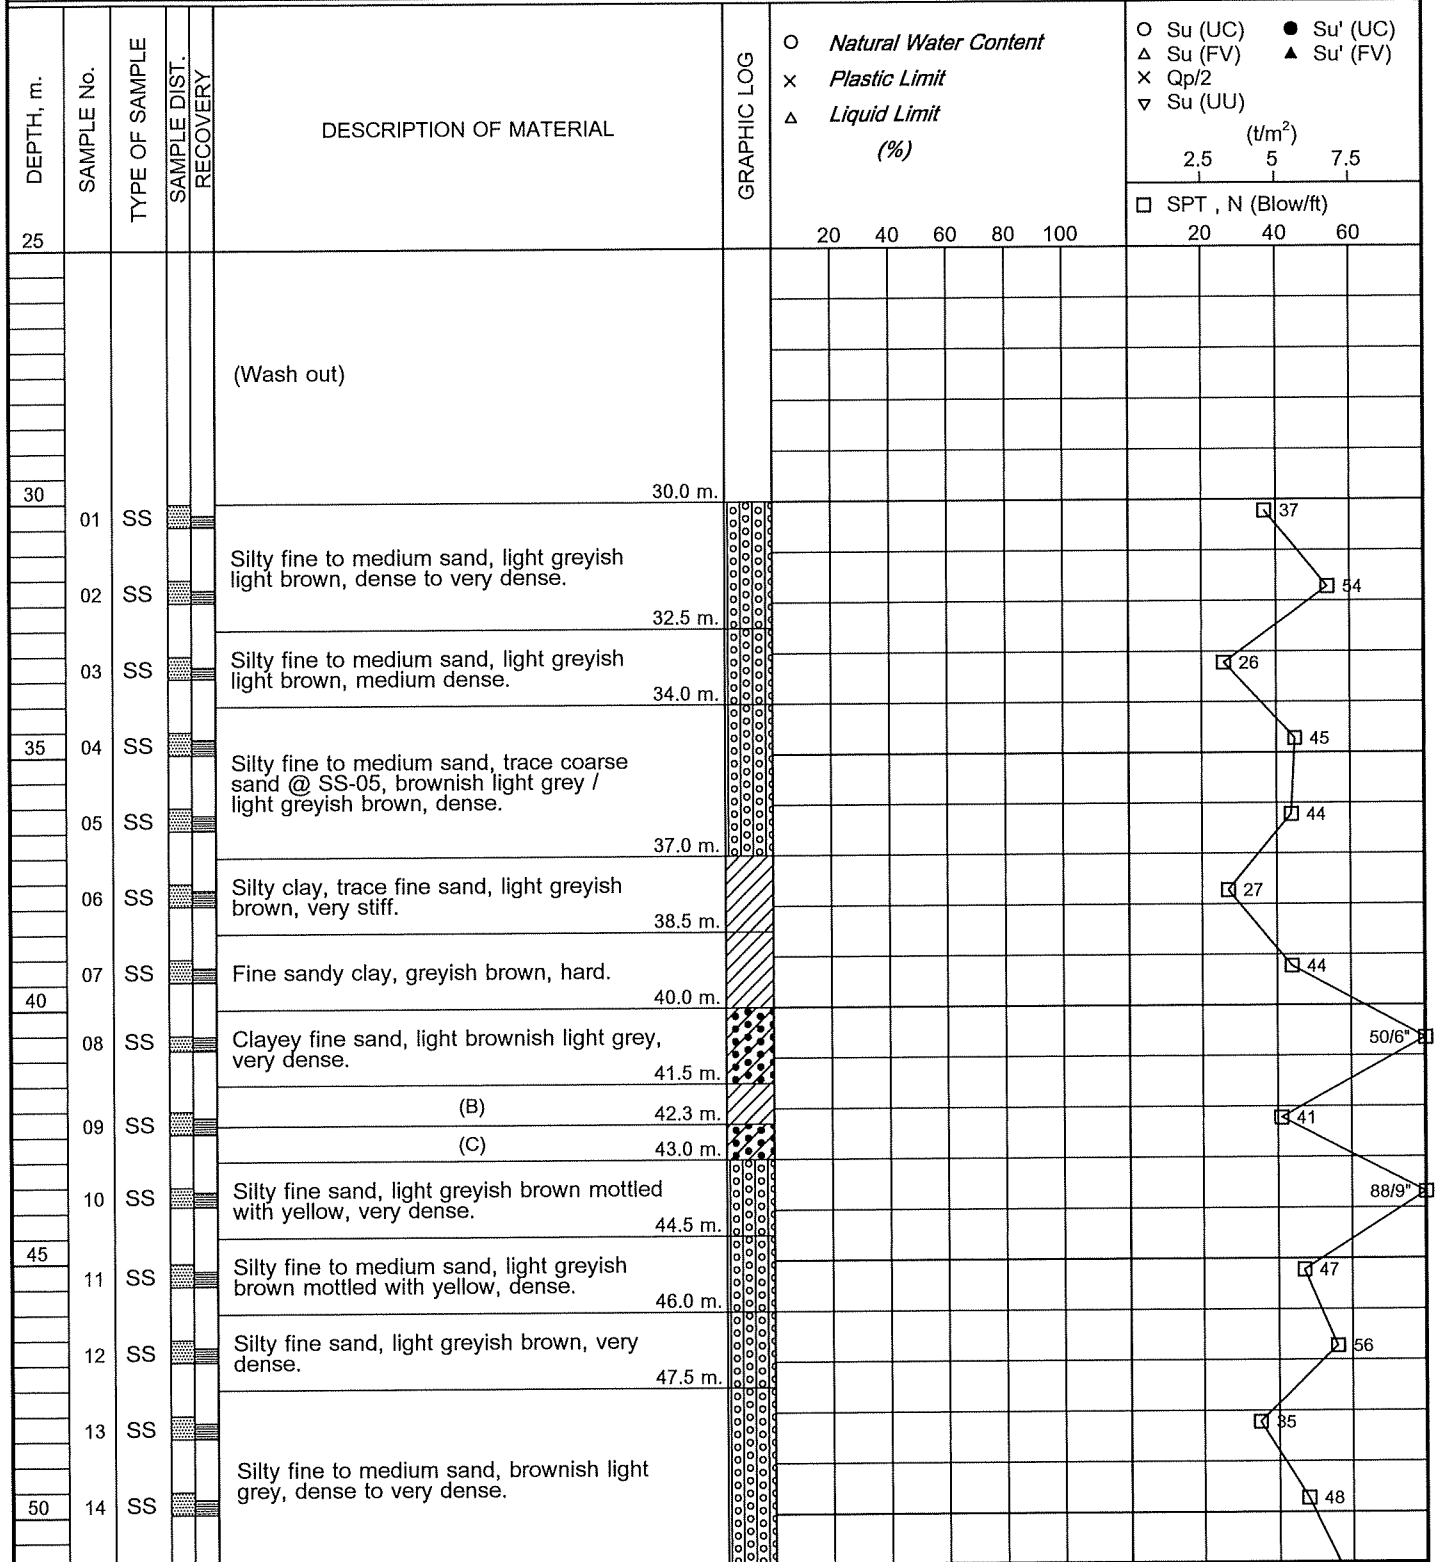

BORING STARTED : 04/03/25

RIG. ACKER

WL. -3.70 m

24 Hrs.
After Boring

BORING FINISHED : 23/01/25

FOREMAN : WN.

JOB No. : 1168049

LOG OF BORING No. OW-34/1

PROJECT : MRT Orange Line Project Bang Khun Non -t						LOCATION : Bangkok													
Min Buri (Suwinthawong) Section Public - Private Partnership Contract																			
DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST.	RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ Natural Water Content					○ Su (UC) ● Su' (UC)							
							× Plastic Limit					△ Su (FV) ▲ Su' (FV)							
						△ Liquid Limit (%)					× Qp/2								
											▽ Su (UU)								
											(t/m ²)								
											2.5 5 7.5								
											□ SPT , N (Blow/ft)								
						20 40 60 80 100					20 40 60								
50																			
	15	SS			Silty fine to medium sand, brownish light grey, dense to very dense. 52.0 m.														58
	16	SS			Silty fine to medium sand, light greyish light brown, dense. 55.0 m.														45
	17	SS																	40
55																			
	18	SS			Silty fine to coarse sand, trace clay pocket, light greyish brown, dense. 56.5 m.														49
	19	SS			Silty fine to medium sand, trace coarse sand, brownish light grey, dense. 58.0 m.														49
	20	SS			Silty fine sand, brownish light grey, very dense. 59.5 m.														84
60																			
	21	SS			(D) 60.45 m.														91
					↑ END OF BORING														
					(A) Concrete plate.														
					(B) Silty clay, trace fine sand seam, brownish light grey, hard.														
					(C) Clayey fine sand, brownish light grey, dense.														
65					(D) Silty fine to medium sand, grey, very dense.														

STS

STS Corp

BORING STARTED : 04/03/25

RIG. ACKER

WL. -3.70 m

24 Hrs. After Boring

BORING FINISHED : 23/01/25

FOREMAN : WN.

JOB No. : 1168049



BORING STARTED : 04/03/25

RIG. ACKER

WL. -3.70 m
24 Hrs. After Boring

BORING FINISHED : 23/01/25

FOREMAN : WN.

JOB No. : 1168049
