


LOG OF BORING No. OW-23/7

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

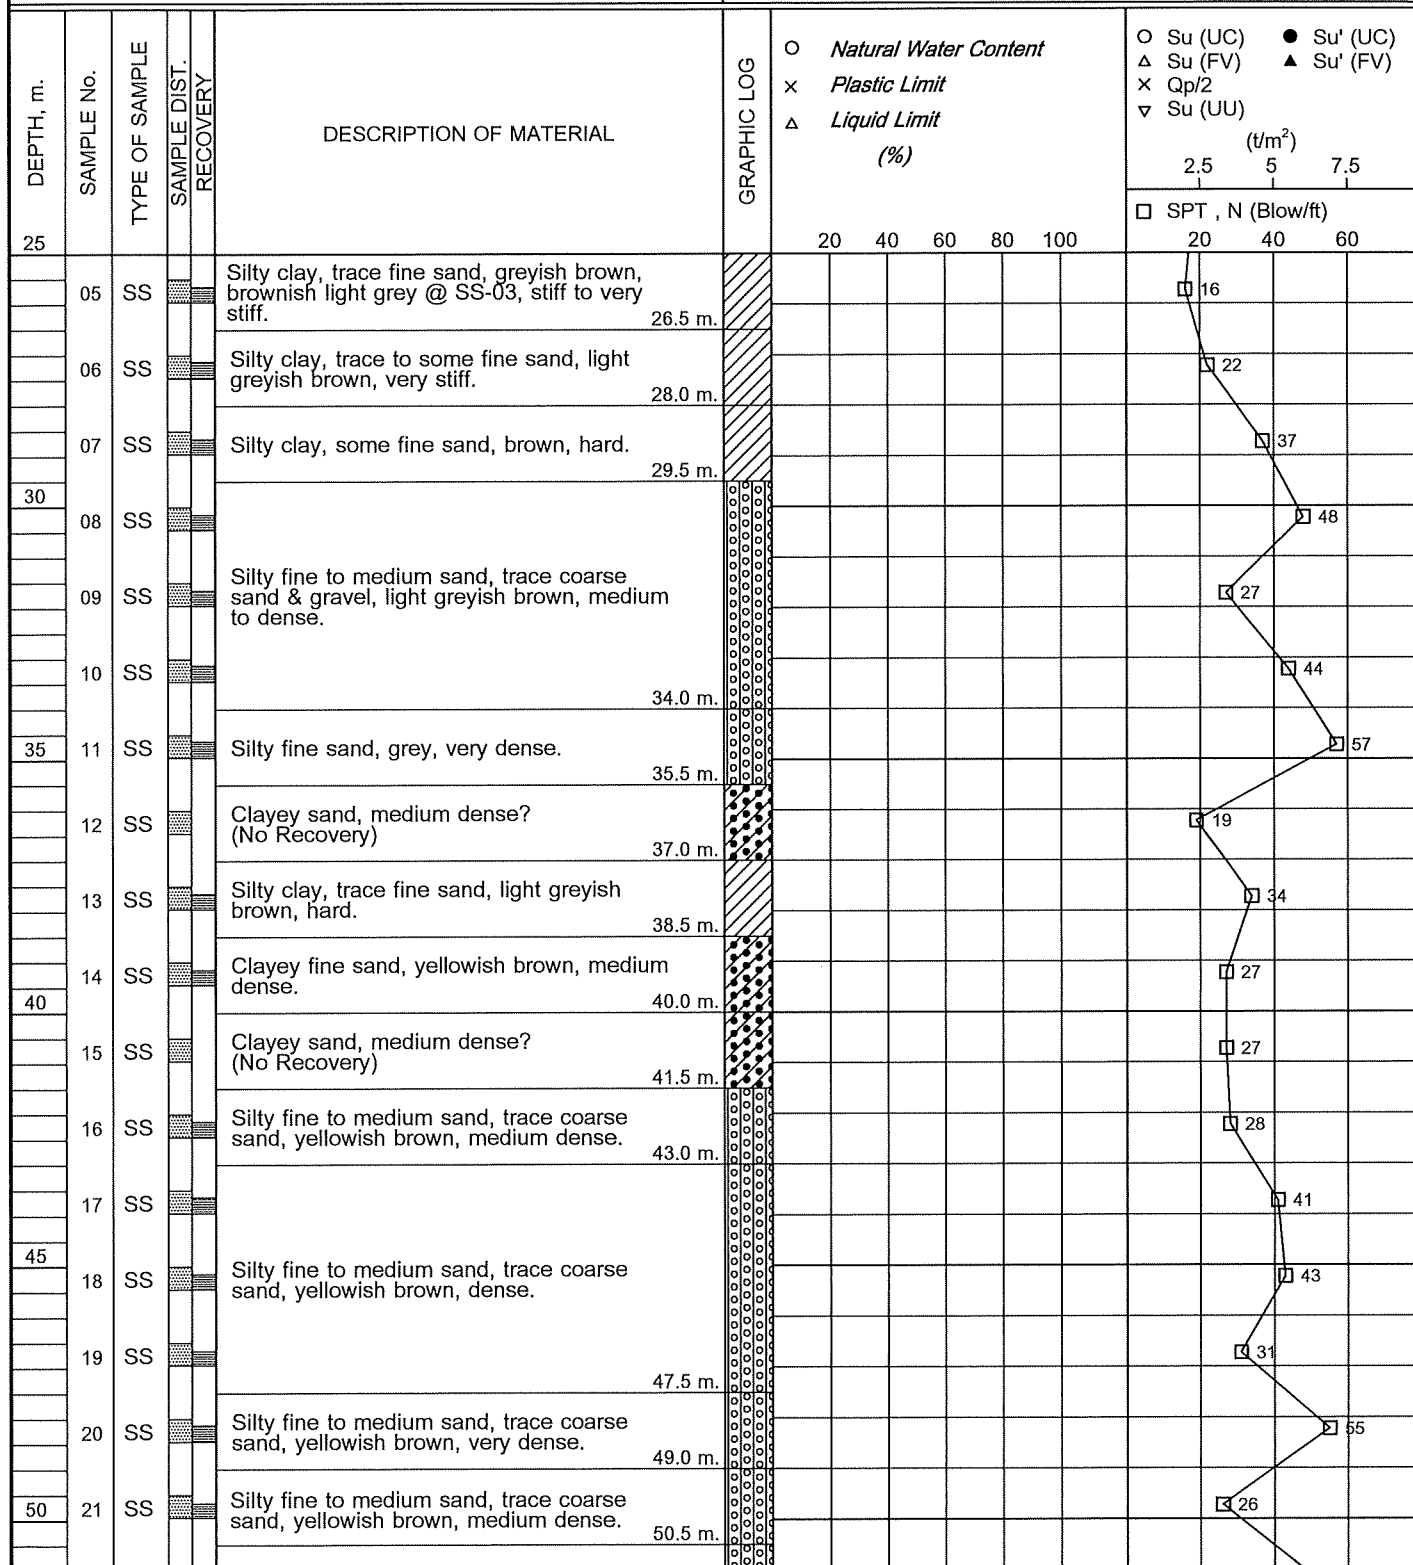

BORING STARTED : 27/03/25

RIG. ACKER

WL. -2.00 m

24 Hrs.
After Boring

BORING FINISHED : 30/03/25

FOREMAN : SJ.


JOB No. : 1168049

LOG OF BORING No. OW-23/7

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

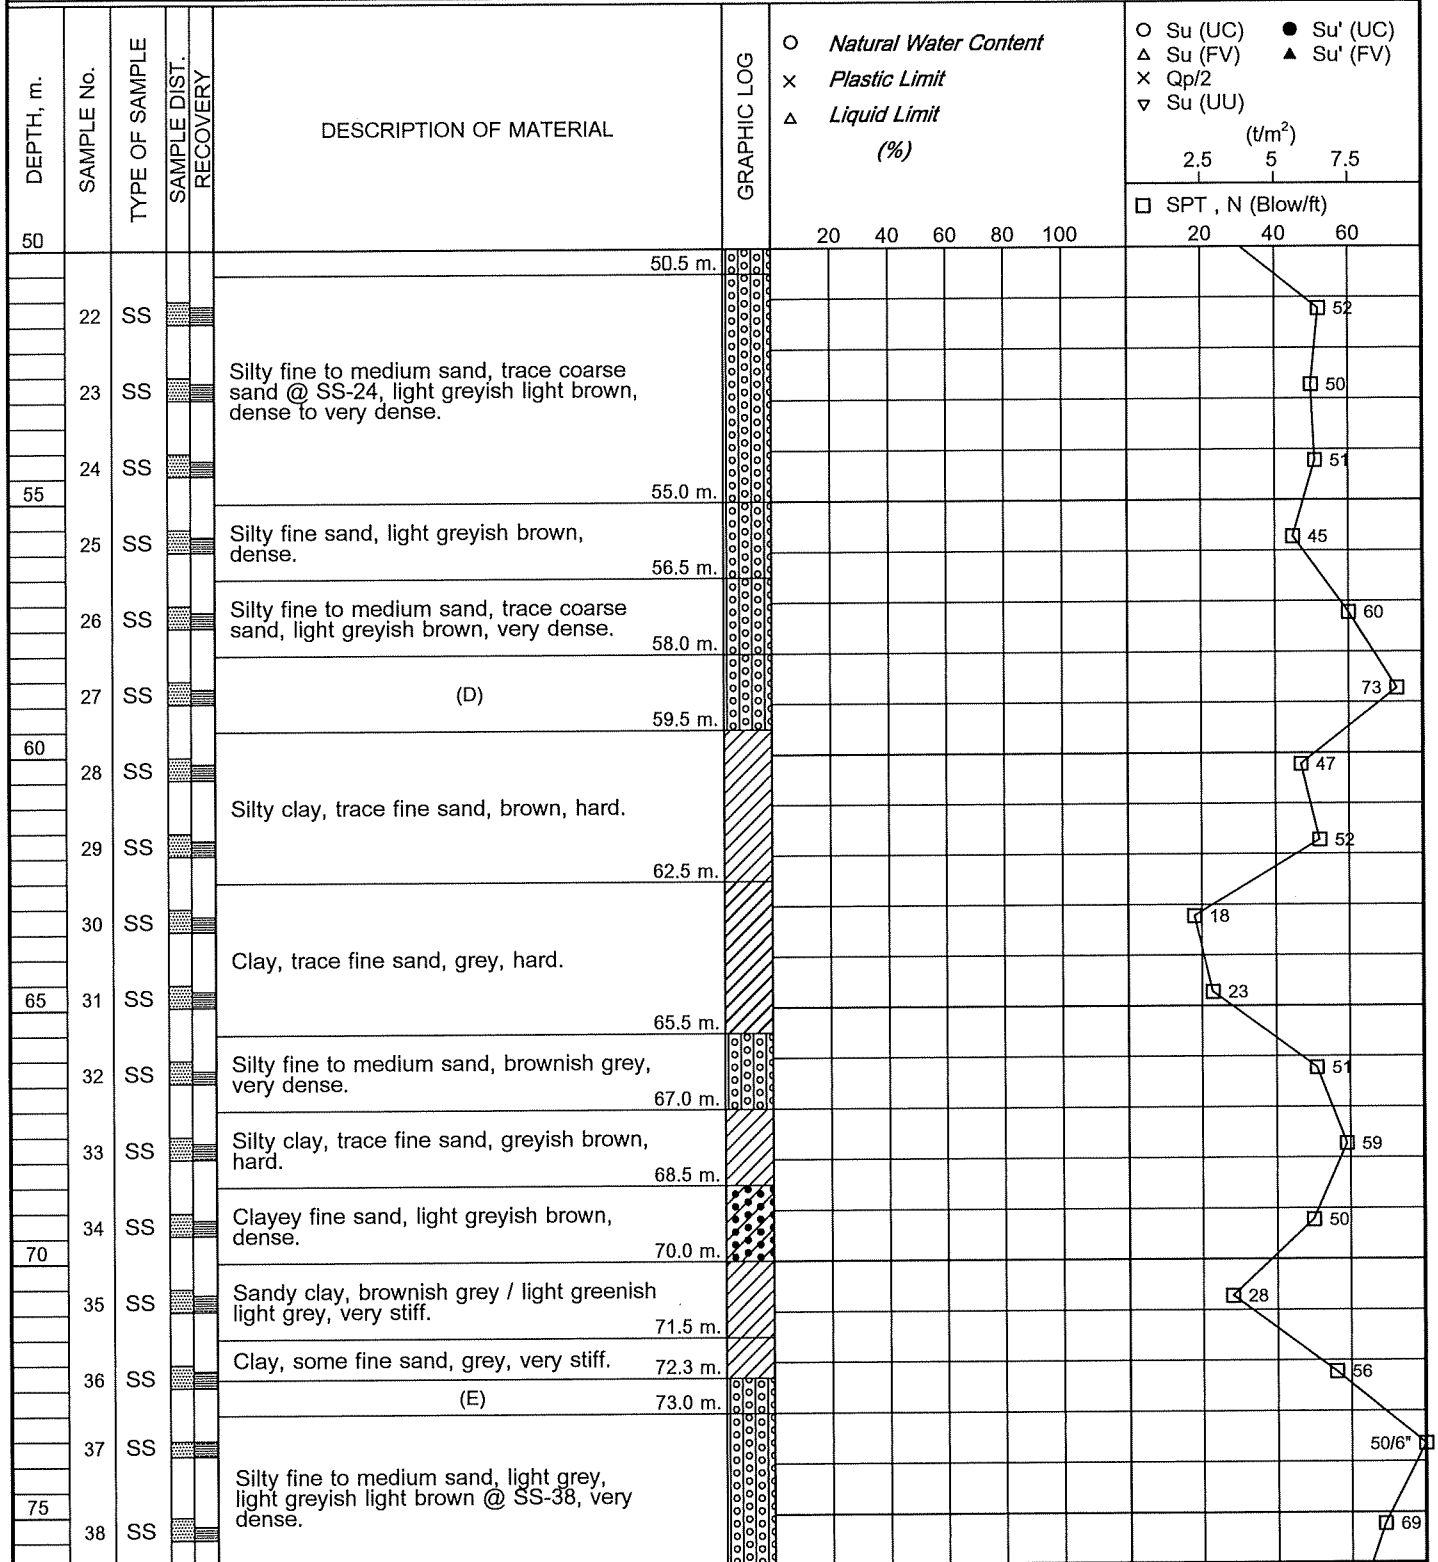

BORING STARTED : 27/03/25

RIG. ACKER

WL. -2.00 m

24 Hrs.
After Boring

BORING FINISHED : 30/03/25

FOREMAN : SJ.

JOB No. : 1168049

LOG OF BORING No. OW-23/7					
PROJECT : MRT Orange Line Project Bang Khun Non -			LOCATION : Bangkok		
Min Buri (Suwinthawong) Section Public - Private Partnership Contract					
DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST. RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG
75					O Natural Water Content x Plastic Limit Δ Liquid Limit (%) ○ Su (UC) △ Su (FV) x Qp/2 ▽ Su (UU) ● Su' (UC) ▲ Su' (FV) (t/m²) 2.5 5 7.5 □ SPT , N (Blow/ft) 20 40 60
	38	SS		Silty fine to medium sand, light grey, light greyish light brown @ SS-38, very dense.	
	39	SS			
				77.5 m.	
	40	SS		Sandy clay, dark grey, stiff.	
				(F) 78.3 m.	
				(G) 79.0 m.	
80	41	SS			
				80.00 m.	
				END OF BORING	
				(A) Asphaltic pavement.	
				(B) Concrete slab.	
				(C) Silty clay, trace fine sand, with lime concretion, light greyish light brown, very stiff.	
85				(D) Silty fine to medium sand, trace to some coarse sand + clay pocket, brown, very dense.	
				(E) Silty fine sand, grey, very dense.	
				(F) Clay, trace fine sand, dark grey, very stiff.	
				(G) Silty fine sand, trace clay pocket, grey, very dense.	
