

LOG OF BORING No. OW-23/8

PROJECT : MRT Orange Line Project Bang Khun Non -					LOCATION : Bangkok					
Min Buri (Suwinthawong) Section Public - Private Partnership Contract										
DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST. RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ Natural Water Content × Plastic Limit Δ Liquid Limit (%) ○ Su (UC) ● Su' (UC) Δ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU) (t/m ²) 2.5 5 7.5 □ SPT, N (Blow/ft) 20 40 60				
0				(A) 0.1 m		20	40	60	80	100
				Silty clay, some fine sand, brown. (Fill) 2.0 m.						
5										
10				(Wash out)						
15										
20	01	SS		(B) 19.5 m.						
				20.5 m.						
	02	SS		Silty clay, trace to some fine sand, light greyish brown, stiff. 22.0 m.						
	03	SS		Silty clay, trace fine sand, greyish brown, very stiff. 23.5 m.						
	04	SS		Silty clay, some fine sand, light greyish brown, stiff to very stiff.						
25										
	05	SS								

STS Corp

BORING STARTED : 06/04/25

BORING FINISHED : 10/04/25

RIG. ACKERT

FOREMAN : RY.

WL. -

JOB No. : 1168049


24 Hrs.
After Boring

LOG OF BORING No. OW-23/8

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

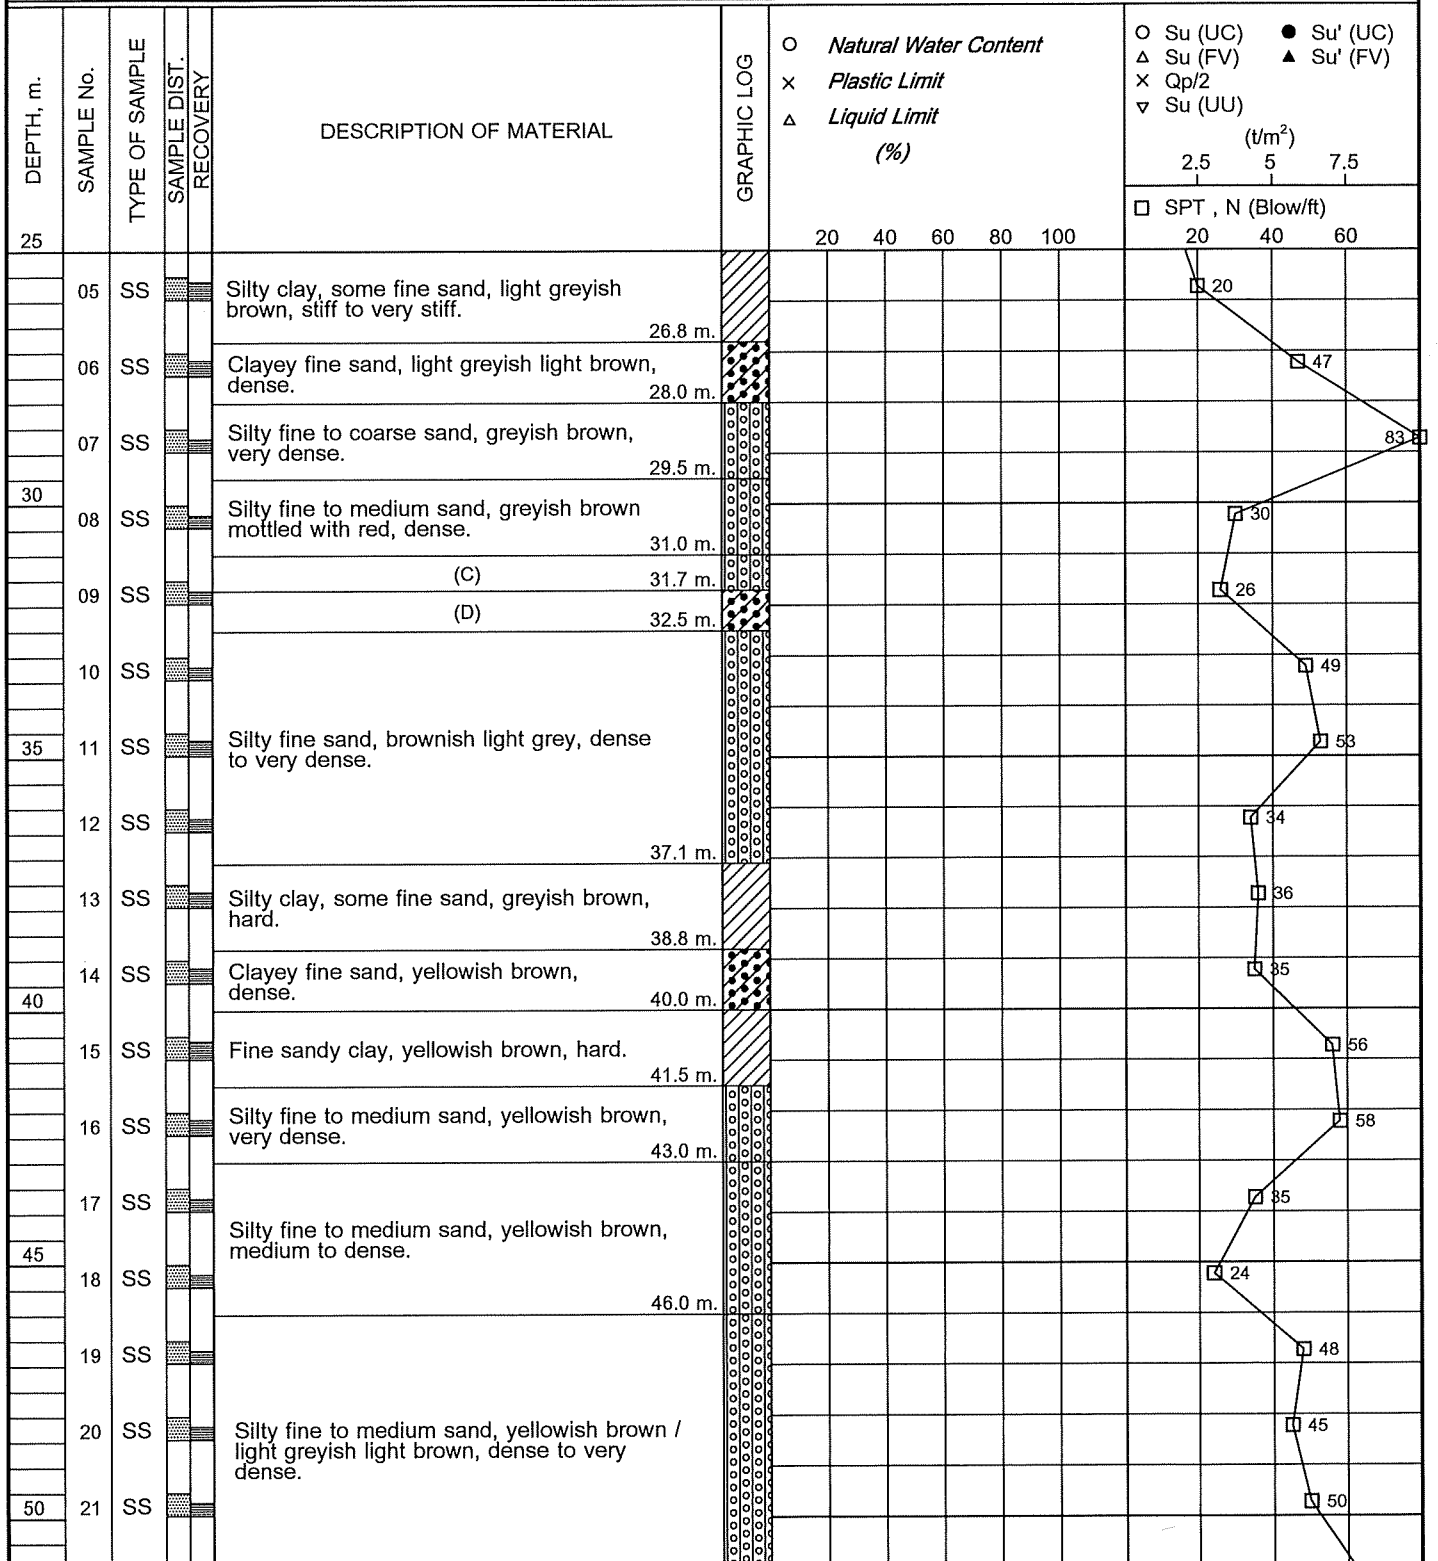

BORING STARTED : 06/04/25

RIG. ACKERT

WL. -

24 Hrs.
After Boring

BORING FINISHED : 10/04/25

FOREMAN : RY.


JOB No. : 1168049

LOG OF BORING No. OW-23/8

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

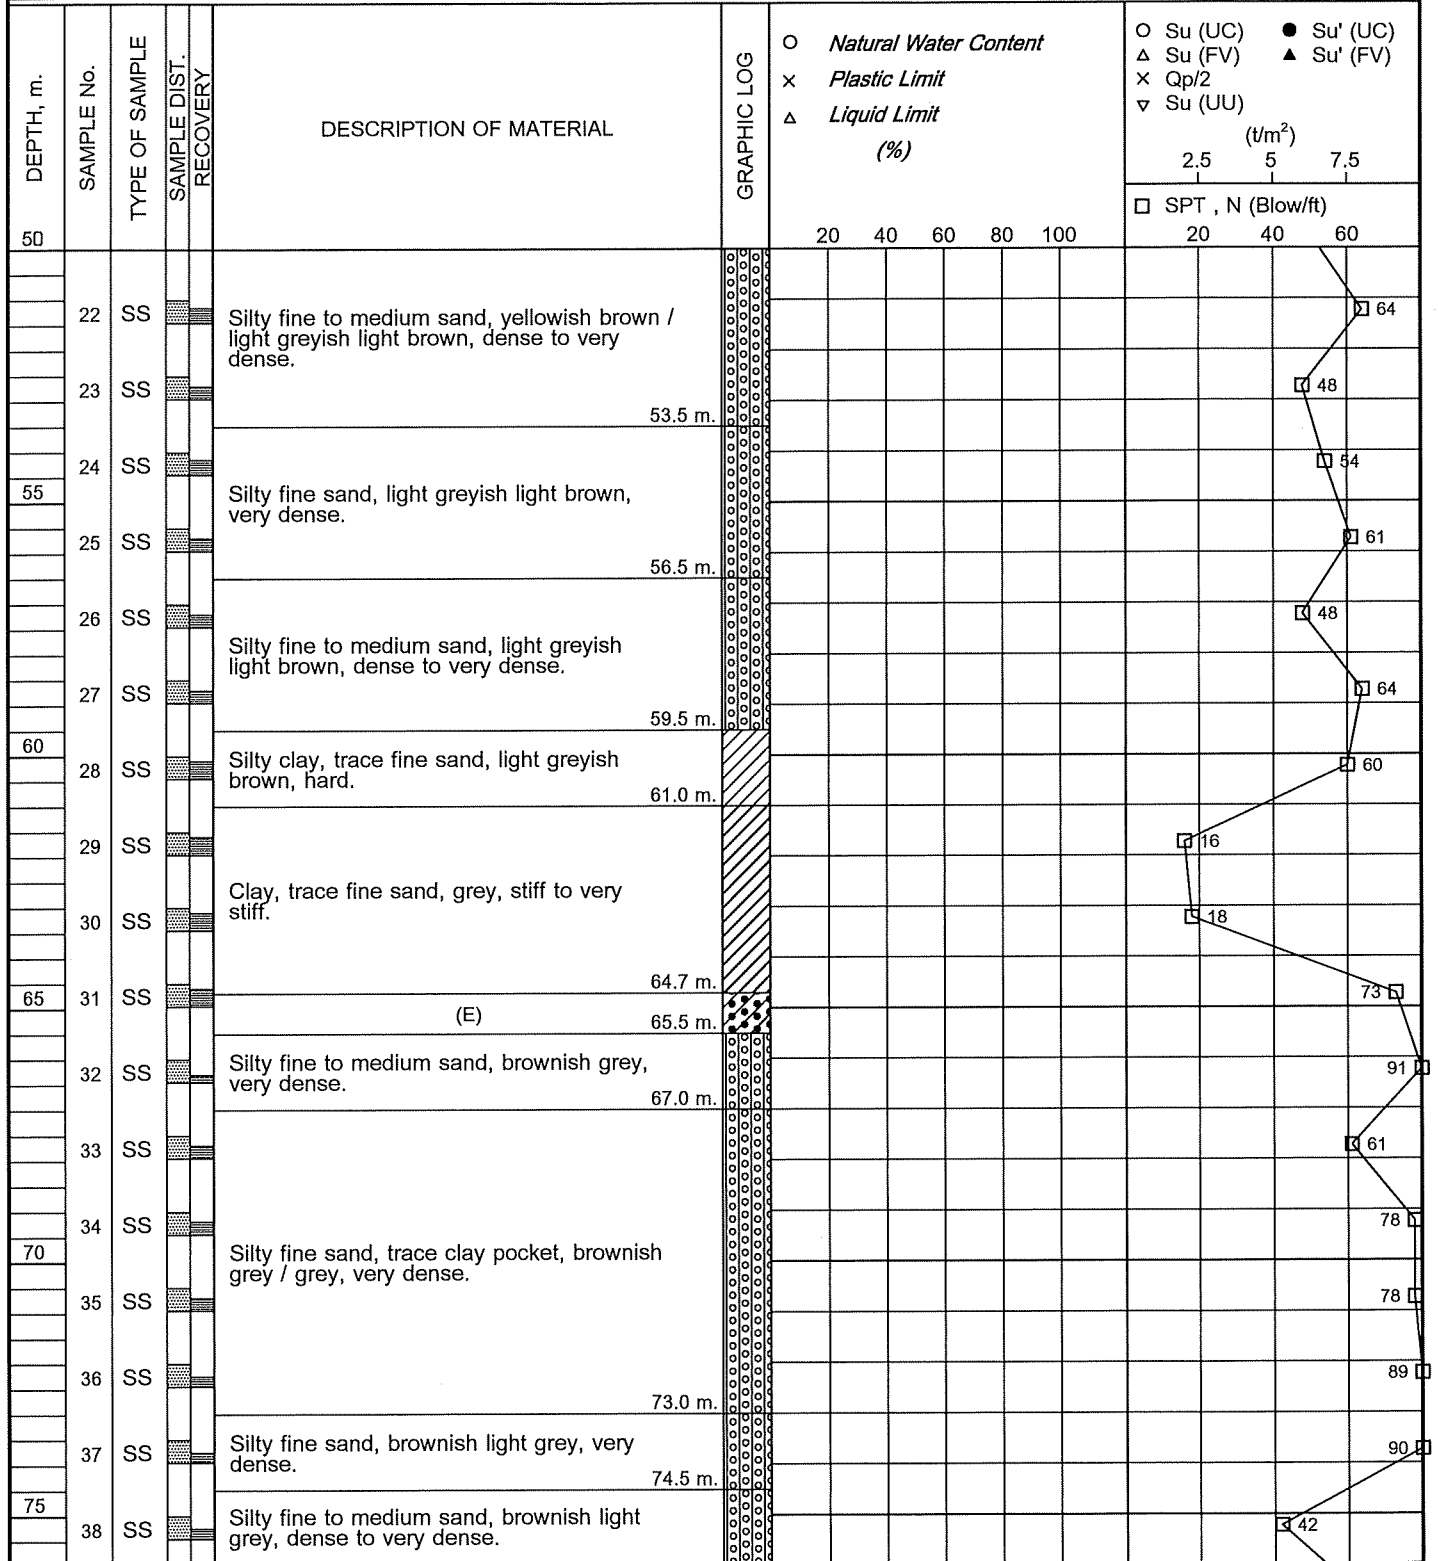

BORING STARTED : 06/04/25

RIG. ACKERT

WL. - 24 Hrs. After Boring

BORING FINISHED : 10/04/25

FOREMAN : RY.

JOB No. : 1168049

LOG OF BORING No. OW-23/8

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST. RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ <i>Natural Water Content</i> × <i>Plastic Limit</i> △ <i>Liquid Limit</i> (%)					○ Su (UC) ● Su' (UC) △ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU) (t/m²) 2.5 5 7.5			□ SPT, N (Blow/ft) 20 40 60		
						20	40	60	80	100	20	40	60	20	40	60
75	38	SS		Silty fine to medium sand, brownish light grey, dense to very dense. 77.5 m.												42
	39	SS														65
	40	SS		Clayey fine sand, grey, very dense. 80.35 m.												95/9"
80	41	SS														98/8"
				END OF BORING												
				(A) Concrete plate.												
				(B) Silty clay, trace fine sand, with lime concretion, brownish light grey, very stiff.												
85				(C) Silty fine to coarse sand, yellowish brown, medium dense.												
				(D) Clayey fine to coarse sand, light greyish brown, medium dense.												
				(E) Clayey sand, grey, very dense.												



BORING STARTED : 06/04/25

RIG. ACKERT

WL. - 24 Hrs. After Boring

BORING FINISHED : 10/04/25

FOREMAN : RY.

JOB No. : 1168049
