

LOG OF BORING No. OW-33/1

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST.	RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ Natural Water Content × Plastic Limit △ Liquid Limit (%)		○ Su (UC) ● Su' (UC) △ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU)			
							(t/m ²)		SPT, N (Blow/ft)			
							2.5	5	7.5	20	40	60
0					(A)	0.2 m.						
5												
10					(Wash out)							
15												
20						20.0 m.						
	01	SS			(B)	20.7 m.						
	02	SS										
	03	SS										
	04	SS										
	05	SS										
	06	SS										
	07	SS										
	08	SS										
	09	SS										
25	10	SS										
	11	SS										
	12	SS										

Silty clay, trace fine sand, trace to some fine sand @ SS-08 & 09, greyish brown, very stiff to hard.

5 32 43 25 21 31 25 26 31 28 23 26


STS Corp

BORING STARTED : 12/11/25 **RIG.** ACKER **WL.** -1.00 m **24 Hrs. After Boring**


BORING FINISHED : 16/11/25 **FOREMAN :** WN. **JOB No. :** 1168286

LOG OF BORING No. OW-33/1

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

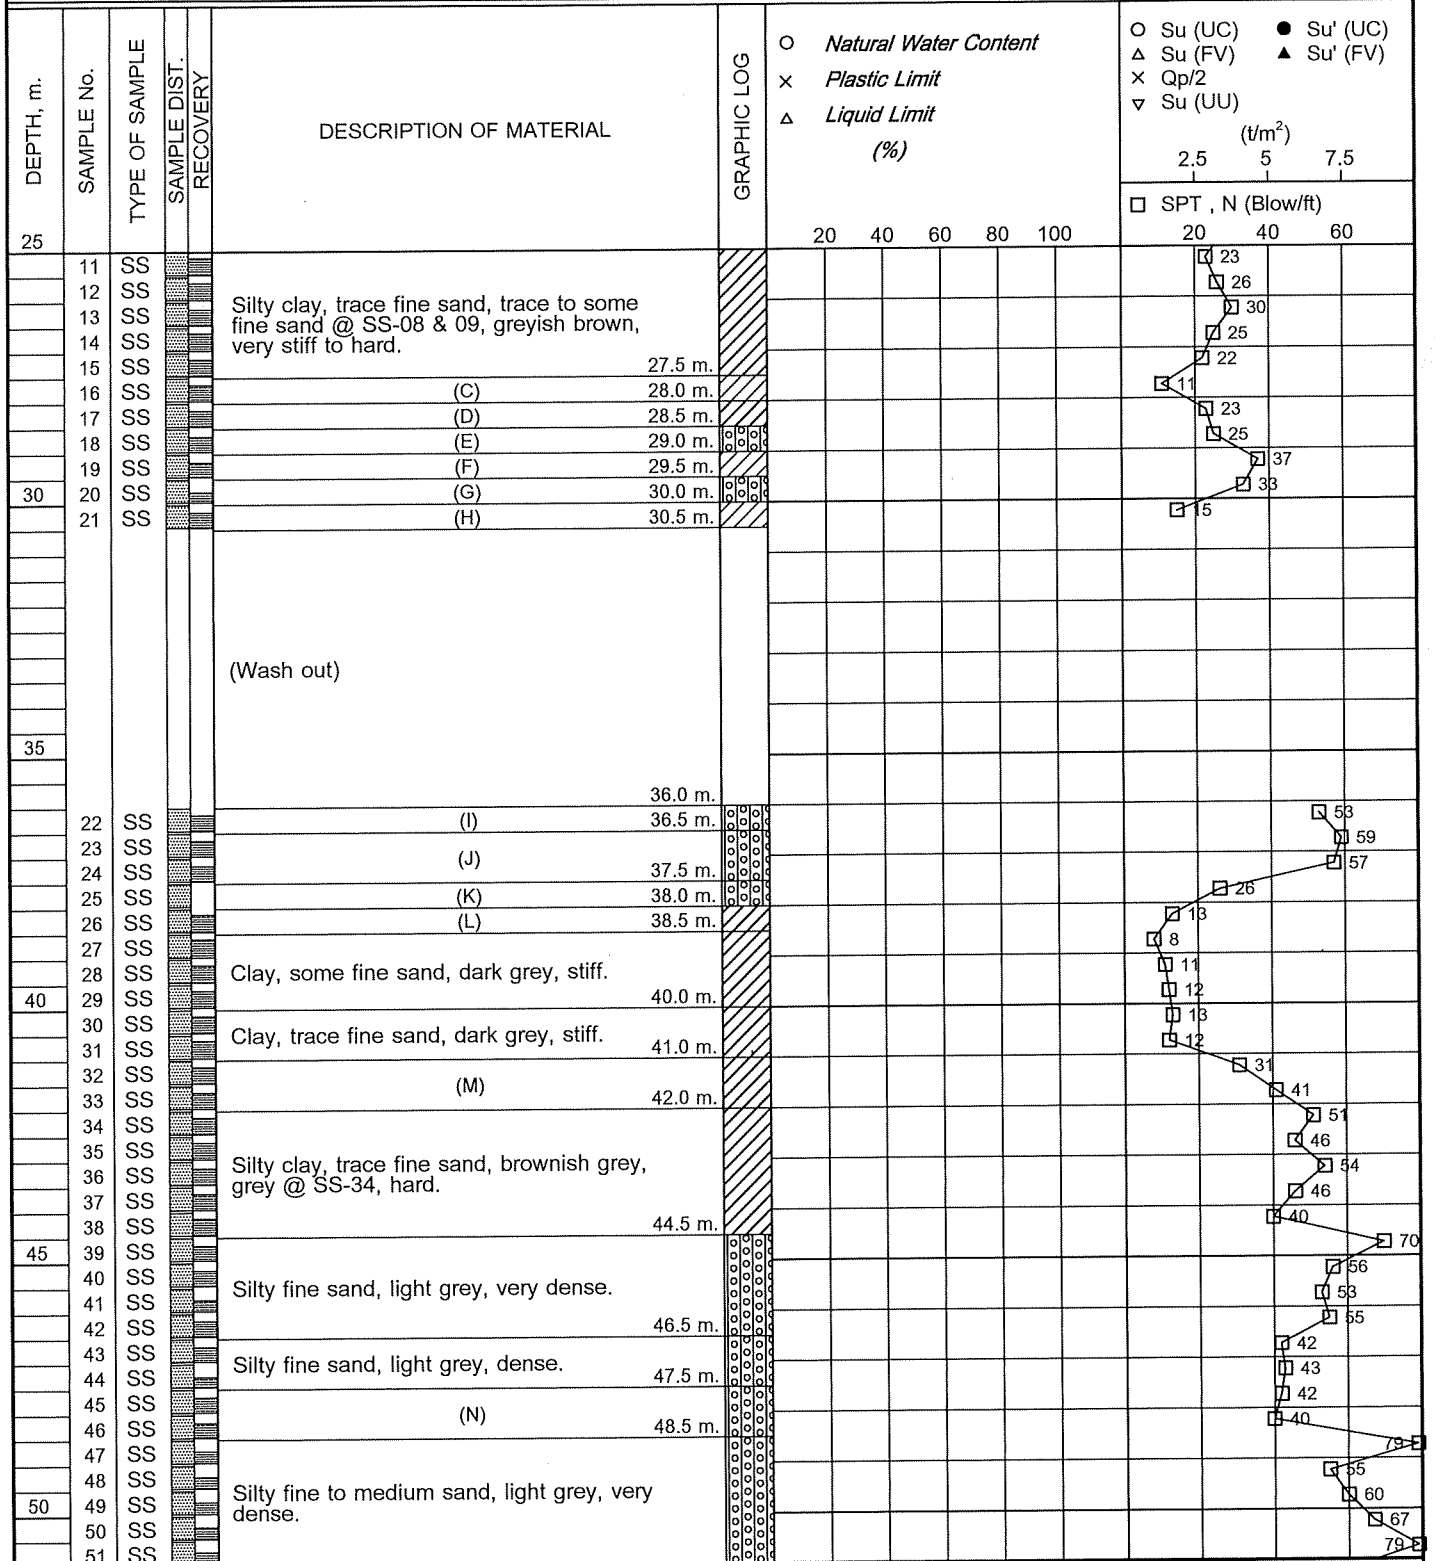

BORING STARTED : 12/11/25

RIG. ACKER

WL. -1.00 m 24 Hrs. After Boring

BORING FINISHED : 16/11/25

FOREMAN : WN.

JOB No. : 1168286

LOG OF BORING No. OW-33/1

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST.	RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ Natural Water Content × Plastic Limit △ Liquid Limit (%)		○ Su (UC) ● Su' (UC) △ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU)		(t/m ²) 2.5 5 7.5 □ SPT, N (Blow/ft) 20 40 60	
50												
	50	SS										
	51	SS			Silty fine to medium sand, light grey, very dense.							67
	52	SS			51.45 m.							58
					↑ END OF BORING (A) Lean concrete. (B) Fine sandy clay, yellowish brown, stiff to very stiff. (C) Silty clay, trace to some fine sand, greyish brown, stiff. (D) Silty clay, trace fine sand, greyish brown, very stiff. (E) Silty fine sand, yellowish brown, medium dense. (F) Fine sandy clay, yellowish brown, hard. (G) Silty fine sand, yellowish brown, dense. (H) Silty clay, some fine sand, greyish brown, stiff. (I) Silty fine sand, trace clay pocket, grey, very dense. (J) Silty fine to medium sand, greyish brown, very dense. (K) Sand, medium dense? (No Recovery) (L) Clay, trace sand, dark grey, stiff. (M) Clay, trace fine sand, grey, very stiff to hard. (N) Silty fine to medium sand, light grey, dense.							
55												

BORING STARTED : 12/11/25
BORING FINISHED : 16/11/25

RIG. ACKER
FOREMAN : WN.

WL. -1.00 m
JOB No. : 1168286

24 Hrs.
 After Boring
