


[illegible]

LOG OF BORING No. OW-34/4

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

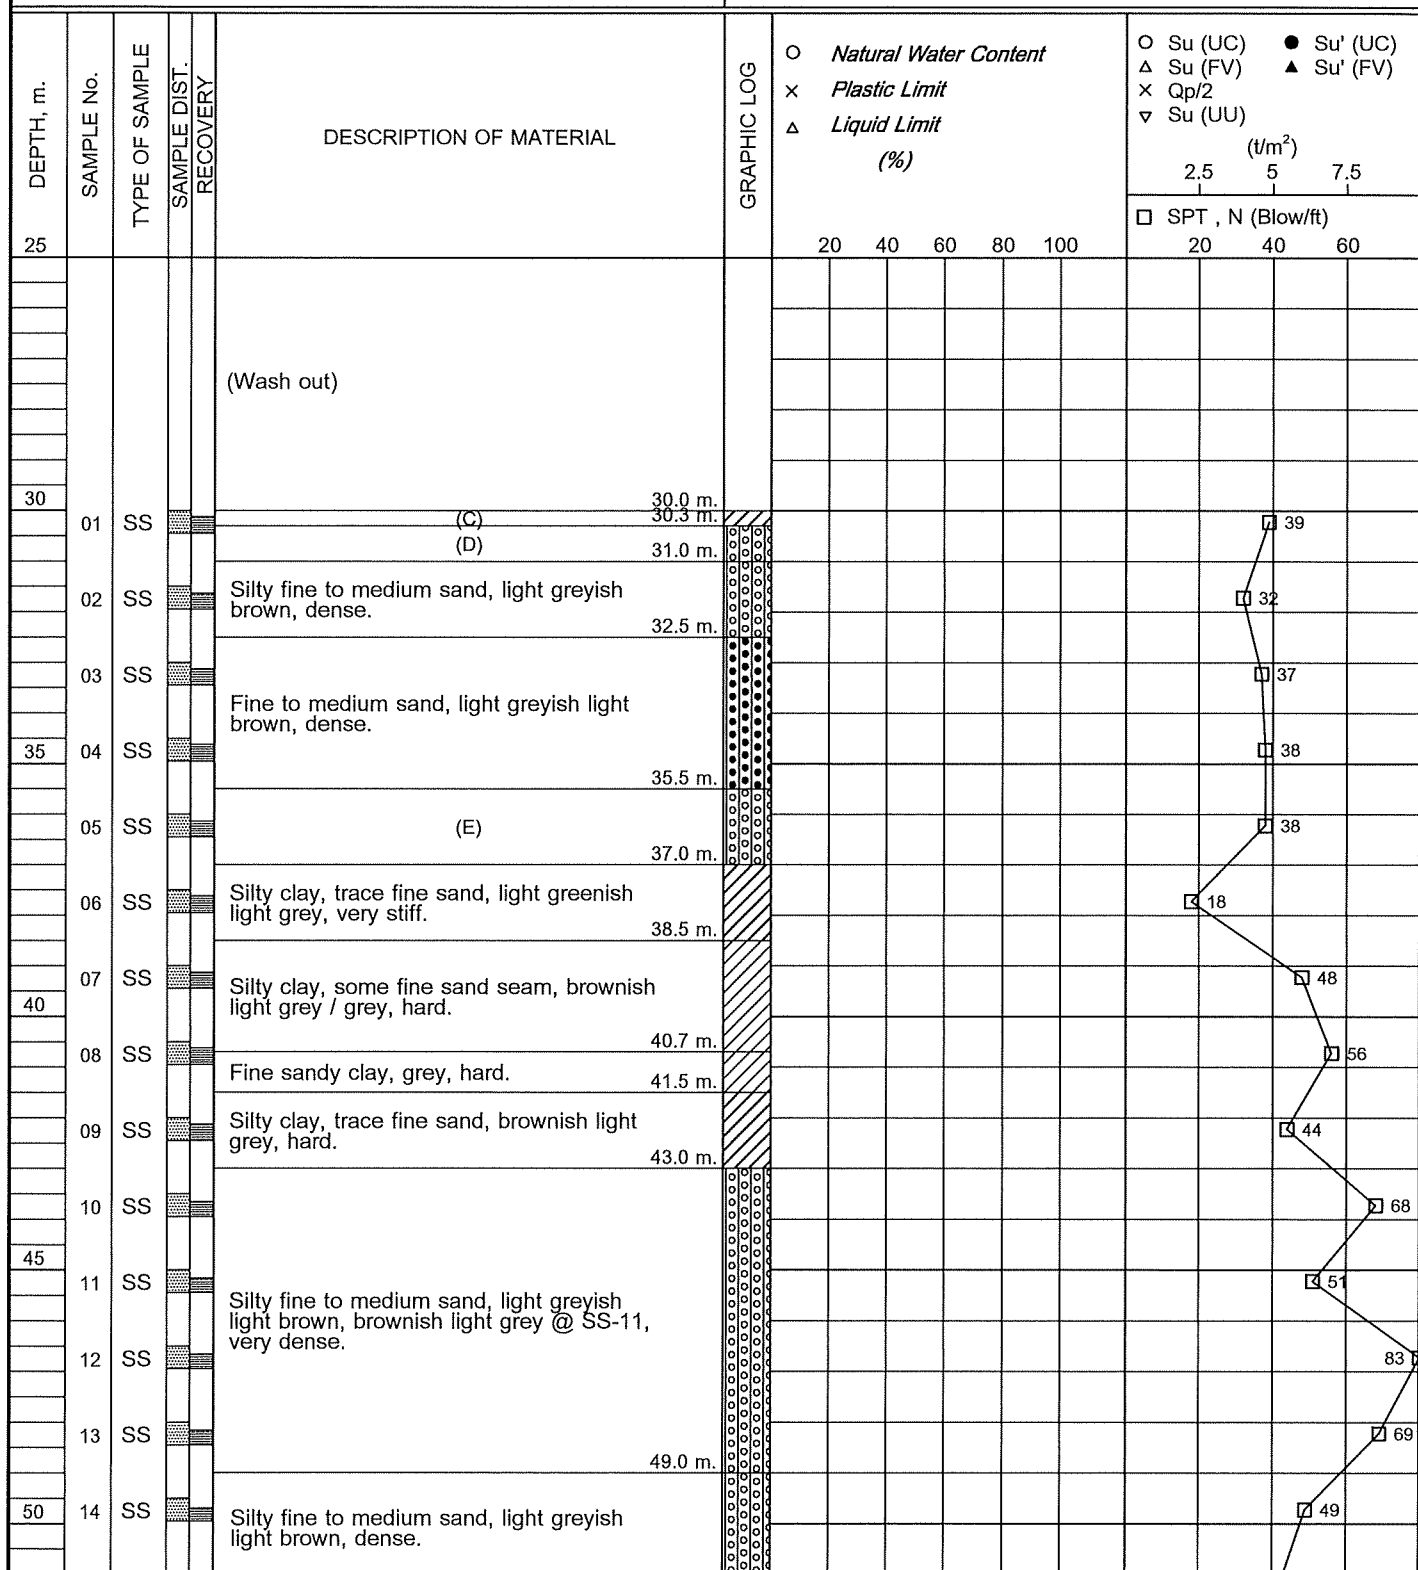

BORING STARTED : 10/06/25

RIG. ACKER

WL. - 3.10 m 24 Hrs. After Boring

BORING FINISHED : 11/06/25

FOREMAN : WN.

JOB No. : 1168049

LOG OF BORING No. OW-34/4

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section Public - Private Partnership Contract

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST. RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	Soil Properties	
						Natural Water Content Plastic Limit Liquid Limit (%)	Su (UC) Su' (UC) Su (FV) Su' (FV) Qp/2 Su (UU)
50						20 40 60 80 100	2.5 5 7.5
15	SS						□ SPT , N (Blow/ft)
16	SS			Silty fine to medium sand, light greyish light brown, dense.			42
17	SS						37
55				55.0 m.			35
18	SS			(F) 55.95 m.			43
				END OF BORING			
60				(A) Concrete plate. (B) Silty fine to medium sand, brown. (Fill) (C) Silty clay, trace fine sand, greyish dark brown, hard. (D) Silty fine sand, brown, dense. (E) Silty fine to medium sand, trace to some coarse sand, light greyish light brown, dense. (F) Silty fine to coarse sand, light greyish light brown, dense.			

BORING STARTED : 10/06/25 RIG. ACKER WL. - 3.10 m 24 Hrs. After Boring

BORING FINISHED : 11/06/25 FOREMAN : WN. JOB No. : 1168049
