

LOG OF BORING No. OW-34/6

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST.	RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ <i>Natural Water Content</i> × <i>Plastic Limit</i> Δ <i>Liquid Limit</i> (%)		○ Su (UC) ● Su' (UC) Δ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU) (t/m ²) 2.5 5 7.5 □ SPT, N (Blow/ft) 20 40 60	
0					(A) 0.3 m.					
5										
10					(Wash out)					
15										
20										
20.0 m.	01	SS			(B)					
21.0 m.	02	SS								
22.5 m.	03	SS			Silty clay, trace fine sand, light greyish brown, very stiff to hard.					
23.5 m.	04	SS								
24.5 m.	05	SS			(C)					
25.0 m.	06	SS								
25.5 m.	07	SS			(D)					
26.0 m.	08	SS								
	09	SS			(E)					
	10	SS								
	11	SS			(F)					
	12	SS			(G)					

BORING STARTED : 22/11/25
BORING FINISHED : 25/11/25

RIG. ACKER
FOREMAN : WN.

WL. - 1.00 m
JOB No. : 1168286


24 Hrs.
 After Boring

LOG OF BORING No. OW-34/6

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

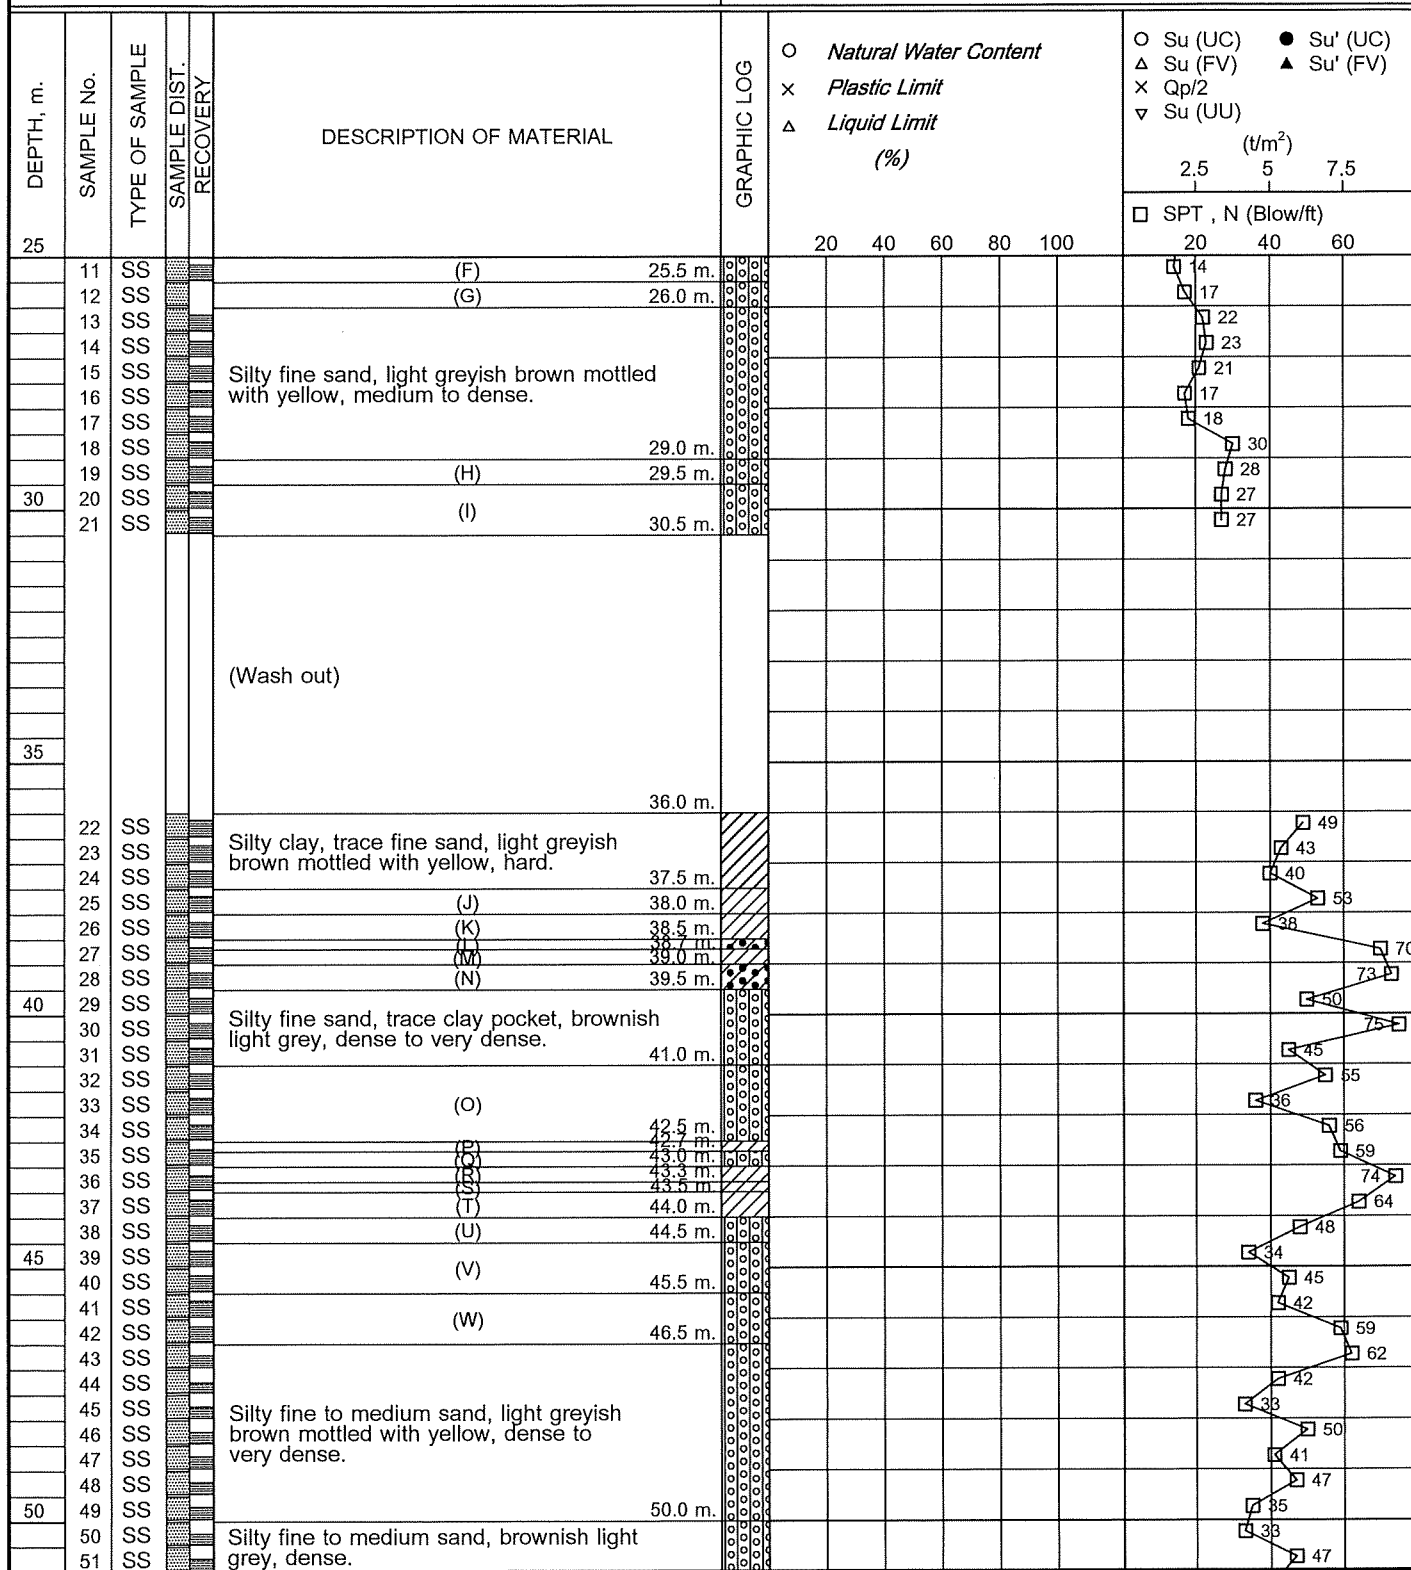

BORING STARTED : 22/11/25

RIG. ACKER

WL. - 1.00 m

24 Hrs.
After Boring

BORING FINISHED : 25/11/25

FOREMAN : WN.

JOB No. : 1168286

LOG OF BORING No. OW-34/6

PROJECT : MRT Orange Line Project Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST.	RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ Natural Water Content × Plastic Limit Δ Liquid Limit (%)		○ Su (UC) ● Su' (UC) Δ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU)								
							(t/m ²)			SPT, N (Blow/ft)							
							20	40	60	80	100	20	40	60			
50	50	SS			Silty fine to medium sand, brownish light grey, dense. 51.45 m.												
	51	SS															
	52	SS															
					END OF BORING												
55					(A) Concrete plate.												
					(B) Silty clay, some fine sand / trace to some fine sand, light greyish brown / brownish light grey, very stiff.												
					(C) Fine sandy clay, light greyish brown, very stiff to hard.												
					(D) Clayey fine sand, brownish light grey, medium dense.												
					(E) Sand, medium dense? (No Recovery)												
					(F) Silty fine sand, brownish grey, medium dense.												
					(G) Sand, medium dense? (No Recovery)												
					(H) Silty fine sand, brownish light grey, medium dense.												
					(I) Silty fine to medium sand, brownish light grey, medium dense.												
					(J) Fine sandy clay, brownish light grey / yellowish brown, hard.												
					(K) Silty clay, some fine sand, light greyish brown, hard.												
					(L) Clayey fine sand, brownish light grey, dense.												
					(M) Silty clay, some fine sand, brownish light grey, hard.												
					(N) Clayey fine sand, light brownish light grey, very dense.												
					(O) Silty fine sand, light greyish light brown / brownish light grey, dense to very dense.												
					(P) Silty clay, trace to some fine sand, yellowish brown, hard.												

BORING STARTED : 22/11/25
BORING FINISHED : 25/11/25

RIG. ACKER
FOREMAN : WN.

WL. - 1.00 m
JOB No. : 1168286

24 Hrs.
 After Boring

