


LOG OF BORING No. OW-38

PROJECT : MRT Orange Line Project : Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

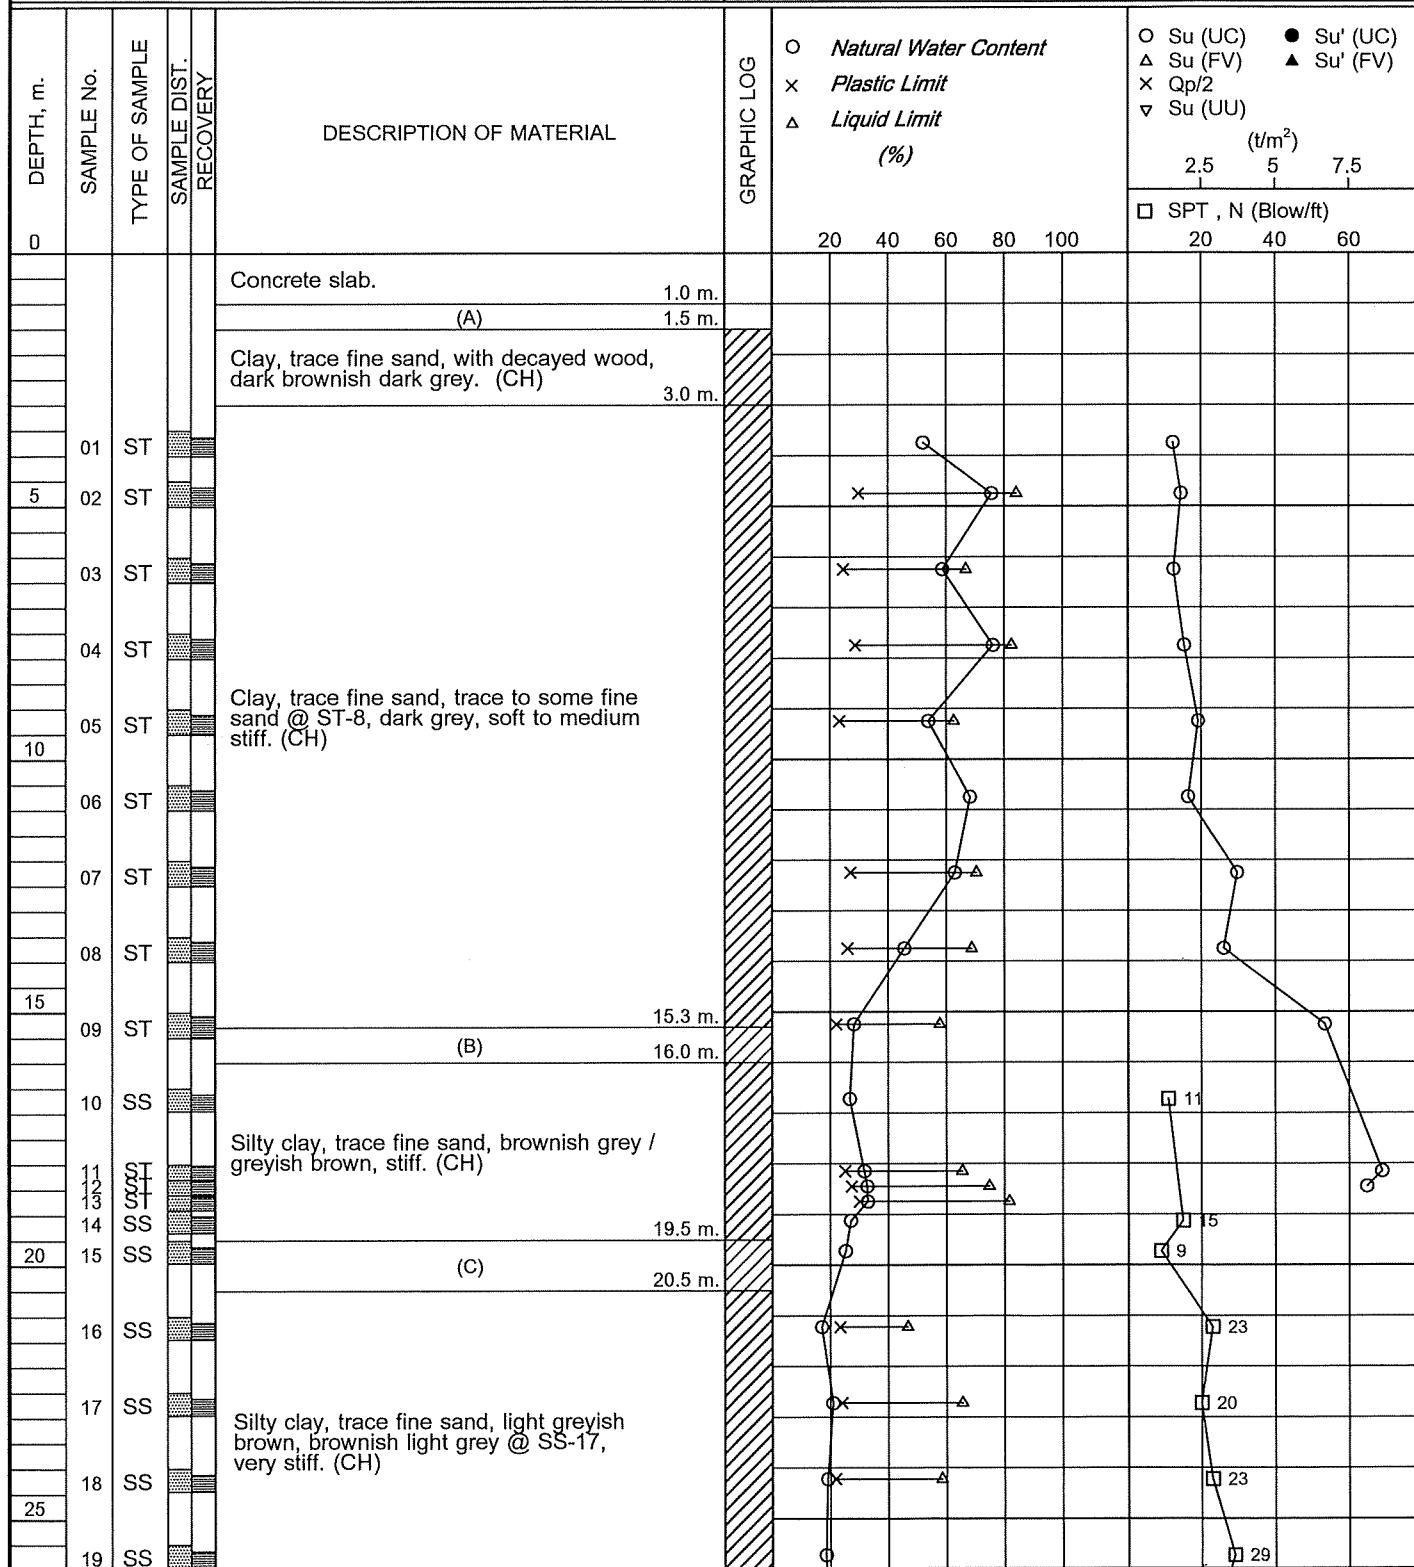

BORING STARTED : 26/10/24

RIG. SUB

WL. ~~1.60 m~~ 24 Hrs. After Boring

BORING FINISHED : 30/10/24

FOREMAN : WN.


JOB No. : 1167287

LOG OF BORING No. OW-38

PROJECT : MRT Orange Line Project : Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

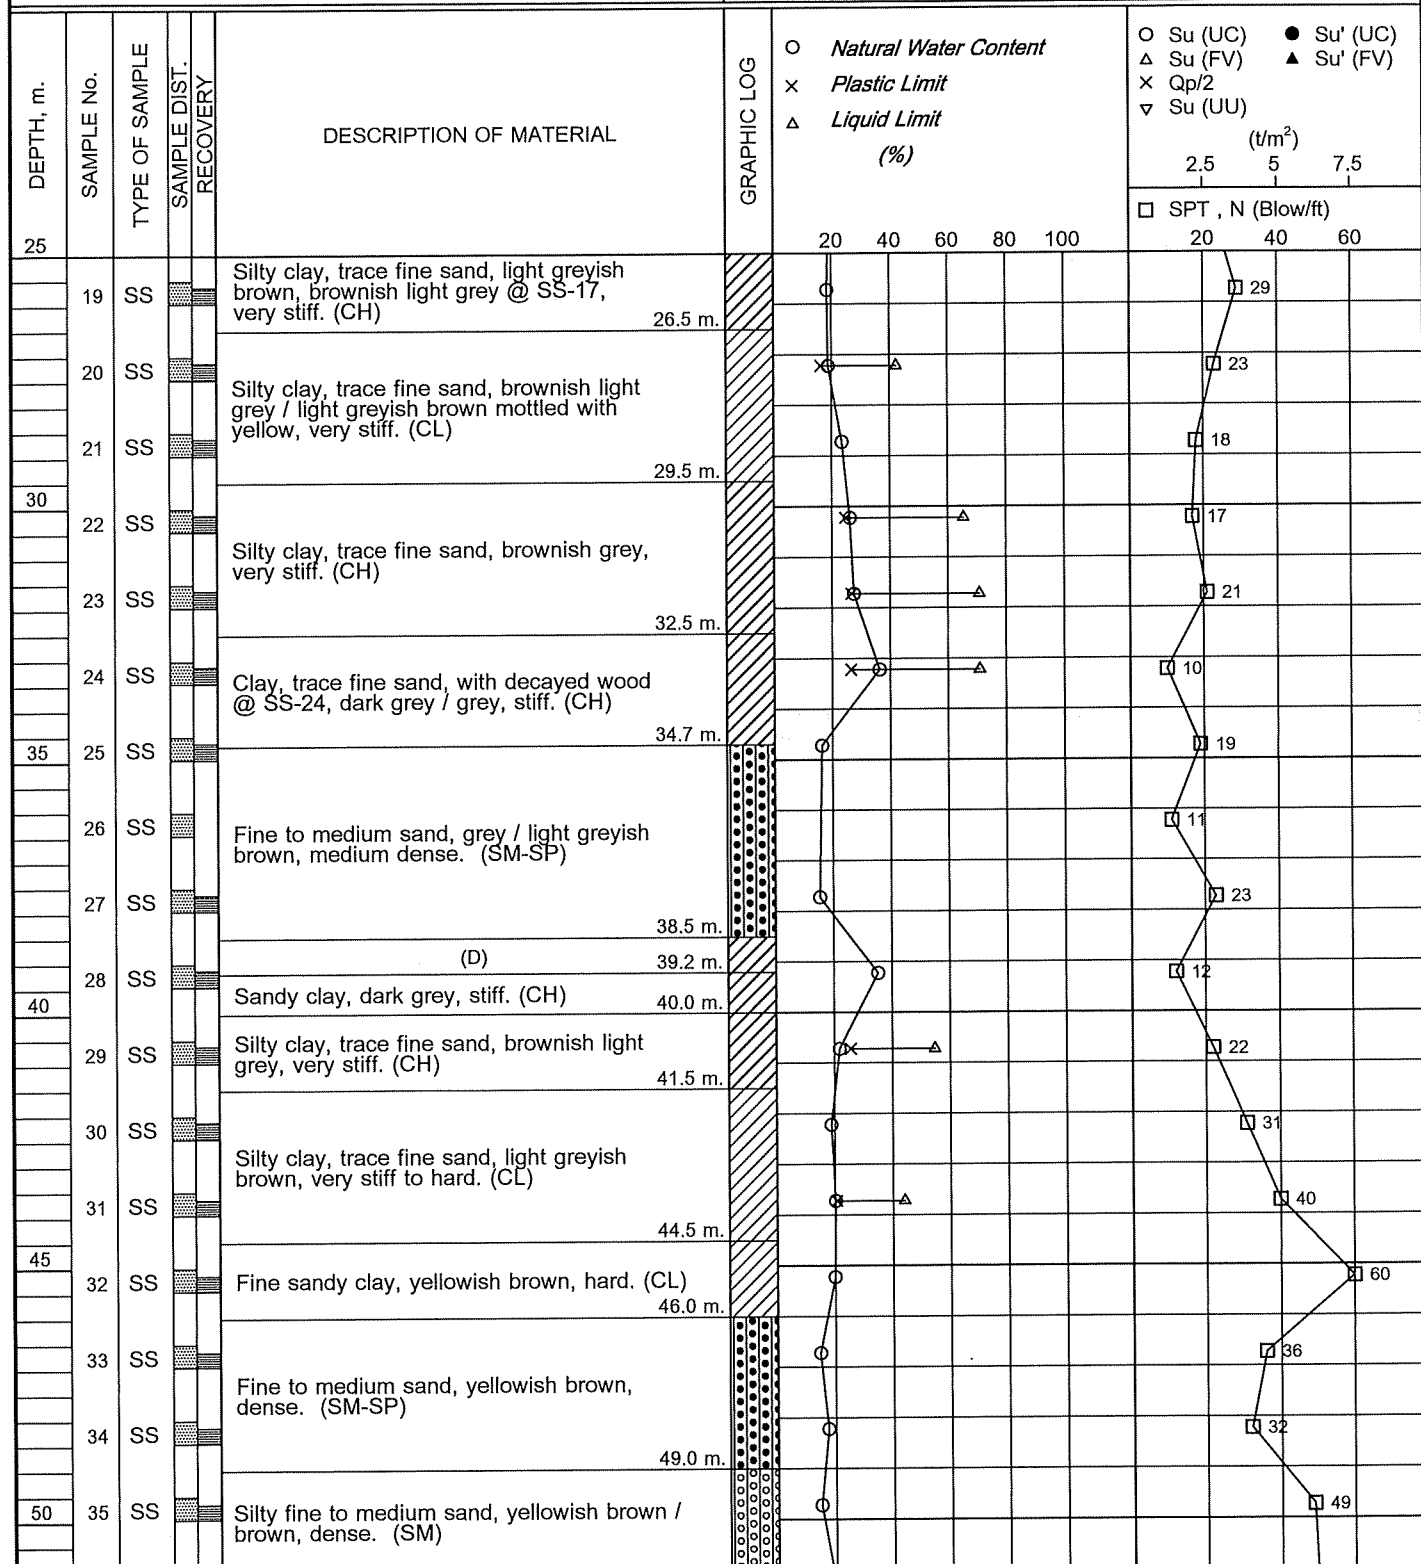

BORING STARTED : 26/10/24

RIG. SUB

WL.

-7.90 m

24 Hrs.
After Boring

BORING FINISHED : 30/10/24

FOREMAN : WN.


JOB No. : 1167287

LOG OF BORING No. OW-38

PROJECT : MRT Orange Line Project : Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

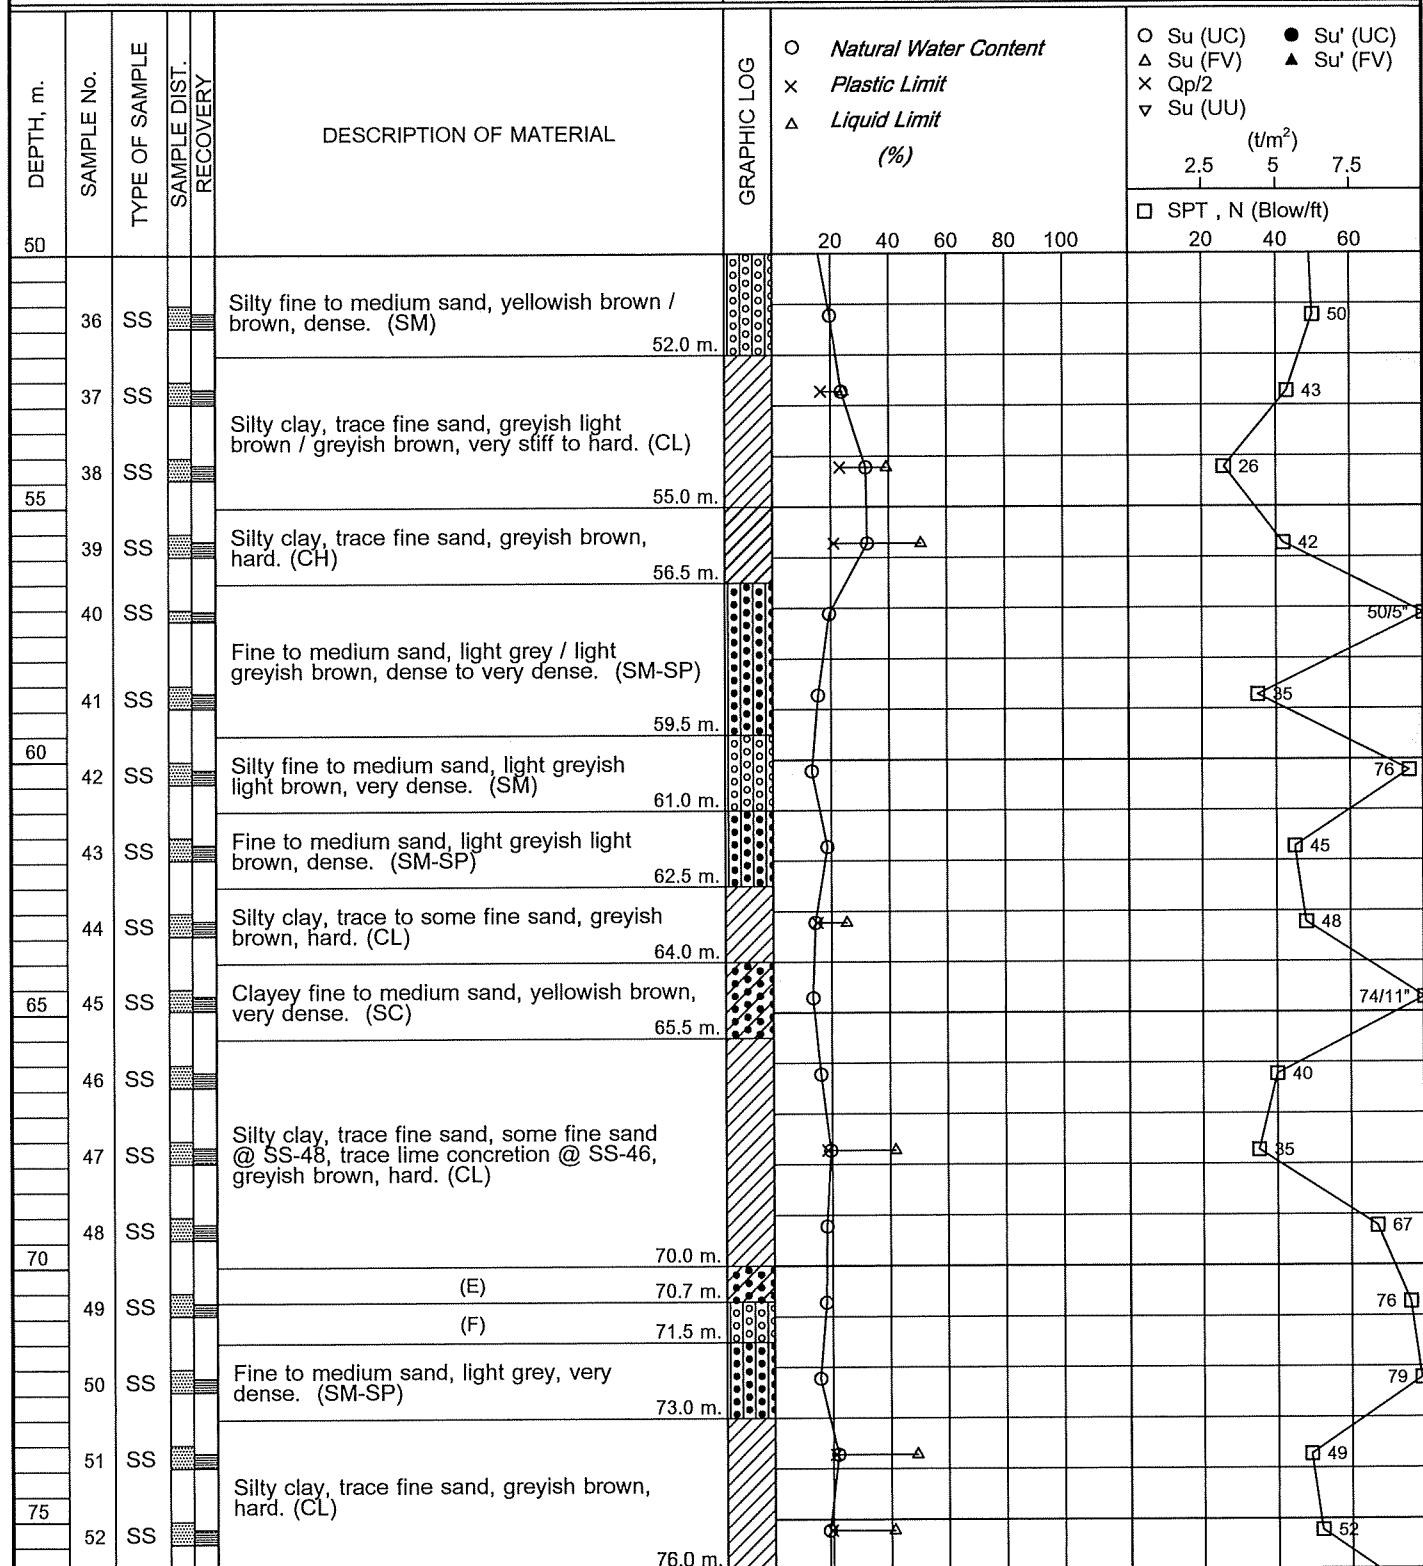

BORING STARTED : 26/10/24

RIG. SUB

WL. -7.90 m

24 Hrs. After Boring

BORING FINISHED : 30/10/24

FOREMAN : WN.

JOB No. : 1167287

LOG OF BORING No. OW-38

PROJECT : MRT Orange Line Project : Bang Khun Non -

LOCATION : Bangkok

Min Buri (Suwinthawong) Section

DEPTH, m.	SAMPLE No.	TYPE OF SAMPLE	SAMPLE DIST. RECOVERY	DESCRIPTION OF MATERIAL	GRAPHIC LOG	○ Natural Water Content × Plastic Limit △ Liquid Limit (%)	○ Su (UC) ● Su' (UC) △ Su (FV) ▲ Su' (FV) × Qp/2 ▽ Su (UU)
75						20 40 60 80 100	2.5 5 7.5 (t/m²) □ SPT, N (Blow/ft) 20 40 60
	52	SS					52
				76.0 m.			
	53	SS		Clayey fine sand, light greyish brown, very dense. (SC)			50/5"
	54	SS					90
				79.0 m.			
	55	SS		(G) 79.73 m.			50/3"
80				END OF BORING			
				(A) Clayey fine sand, brownish grey to dark grey. (Fill)			
				(B) Gravelly sandy clay, light greenish light grey, stiff. (CL)			
85				(C) Silty clay, some fine sand, yellowish brown, stiff. (CL)			
				(D) Clay, trace to some fine sand, dark grey, stiff. (CH)			
				(E) Clayey fine sand, light grey, very dense. (SC)			
				(F) Silty fine sand, light grey, very dense. (SM)			
				(G) Silty fine sand, grey, very dense. (SM)			



BORING STARTED : 26/10/24

RIG. SUB

WL. -7.90 m 24 Hrs. After Boring

BORING FINISHED : 30/10/24

FOREMAN : WN.

JOB No. : 1167287
